

# PARKMORE BUS PRIORITY SCHEME

## NEWSLETTER - ISSUE NO. 4


29<sup>th</sup> March 2024

### **WELCOME TO THE 4<sup>th</sup> ISSUE OF THE PARKMORE BUS PRIORITY SCHEME NEWSLETTER**

Construction of the Parkmore Bus Priority scheme has been ongoing since the 19<sup>th</sup> February with good progress being made on works at Monivea Junction, Parkmore Road and Ballybritt Crescent. The following gives an outline of works planned for the next 4 weeks:-

#### **Day shift works:**

- Works on the Eastern Footpath, Stage 3 area highlighted in (blue) will continue for the next 4 weeks. Works will be concentrated on kerb installation and concrete footpath finishing works. Once finishing works is complete in Stage 3 it is planned switch over to finishing works on the opposite footpath in Stg 2 Area.
- Main Storm drain and ducting works is complete in Stages 1-4 and is progressing into Stage 5.
- Temporary traffic management measures, including off peak lane closures and temporary pedestrian and cycleway diversions, will also be in place around the works areas as is necessary.
- Works will be carefully planned and sequenced in stages to minimise traffic disruption.

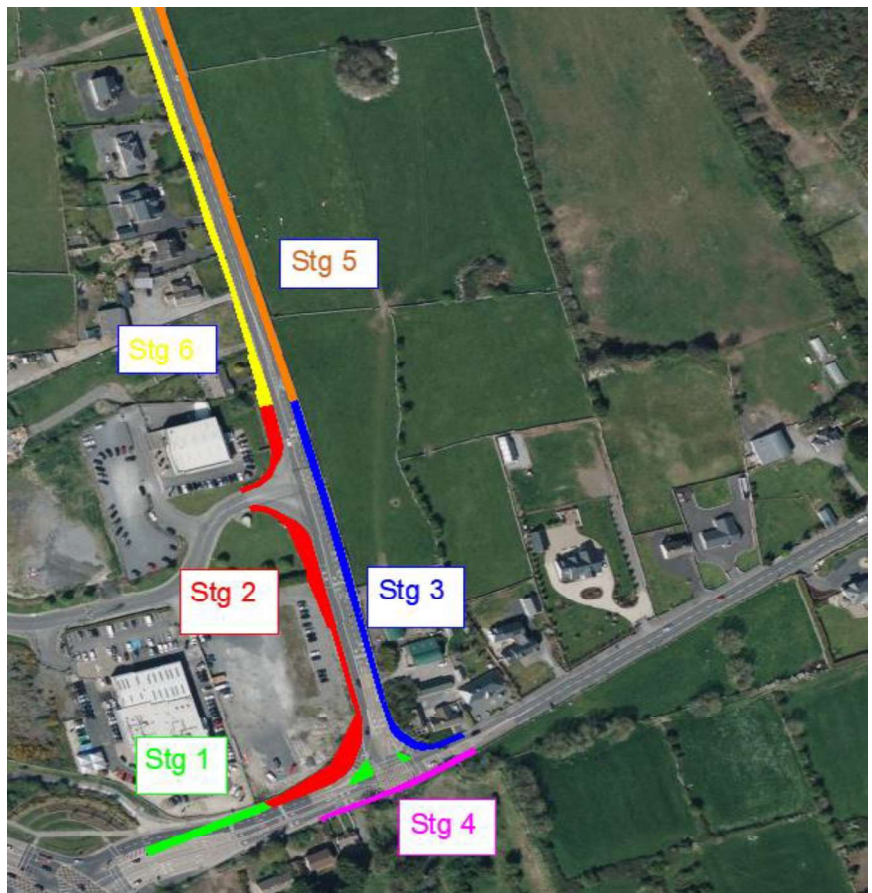

#### **Night shift works:**


- Night shift works will be ongoing in Stage Areas 5 and 6 from the 8<sup>th</sup> April to 3<sup>RD</sup> May.
- Night shift works will run from 6:30pm in the evening to approximately 6.00am the following morning.
- Temporary traffic management measures, including some lane closures, will be required from the Briarhill Junction to Parkmore Road to facilitate the works.
- Temporary pedestrian and cycleway diversions will also be in place around the works areas as is necessary.

## Easter Holiday Works:

- JCEL plan to continue works over the Easter period as traffic volumes will be reduced. Dayshift works will be carried out from the Tuesday the 2<sup>nd</sup> to Friday the 5<sup>th</sup> April.

## Ballybritt Crescent Works (Dayshift) Works:

- Works is progressing in the Ballybritt Crescent area (Highlighted in **Pink**) with attenuation tank installation, bulk earthworks and drainage and ducting works 95% complete.
- Works over the coming 4 weeks will focus on kerb and gully installation, bus shelter installation and footpath finishing works.
- Landscaping and is planned to be completed in late April/Early May, weather dependent.
- Both entrances to Ballybritt crescent will be maintained for the majority of works, but there will be periods where one entrance will need to be closed to facilitate construction of the new pedestrian crossings.

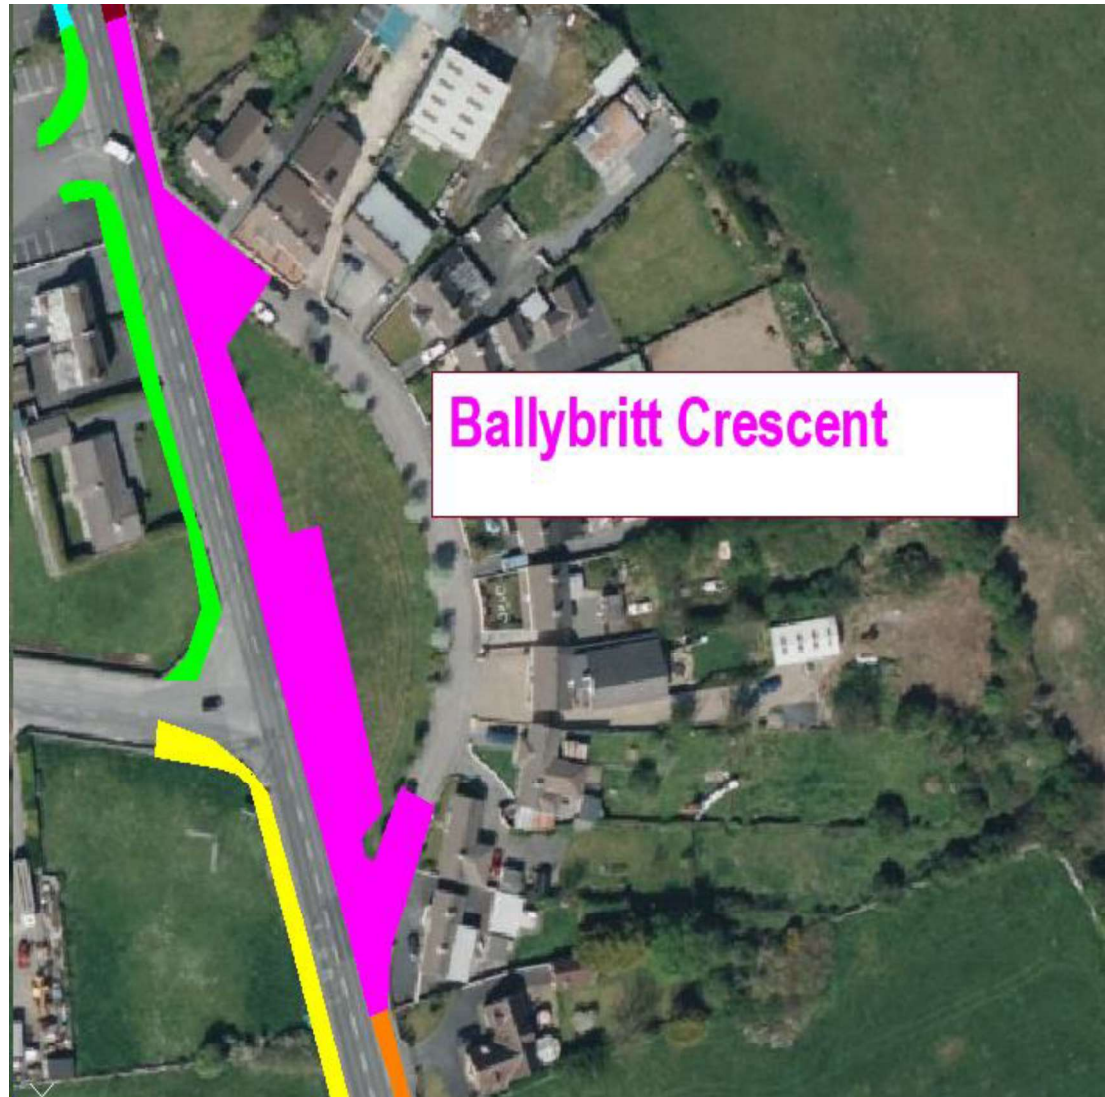

**For further information:** Contact us at Jons Civil Engineering 0860835461 or [donalkelly@jonscivil.ie](mailto:donalkelly@jonscivil.ie)
